

Project update

28 June 2024

Pier Pavilion

A spectacular public landmark is coming. Pier Pavilion, located in Watermans Cove, will be a stunning public space where people can shelter, meet, gather and relax by the water. Infrastructure NSW has engaged Stephen Edwards Constructions (SEC) to deliver the works.


Works update

Construction of the steel structure has progressed to 100%. The 'oculus' has been installed, completing the steel roof structure. The oculus is a feature of the design, located in the centre of the pavilion and will let sunlight into the space.

Scaffolding has been installed around the perimeter of the steel structure, in preparation of the upcoming roof works required to install a green roof on the pavilion.



Above: Installation of the steel structure is now complete

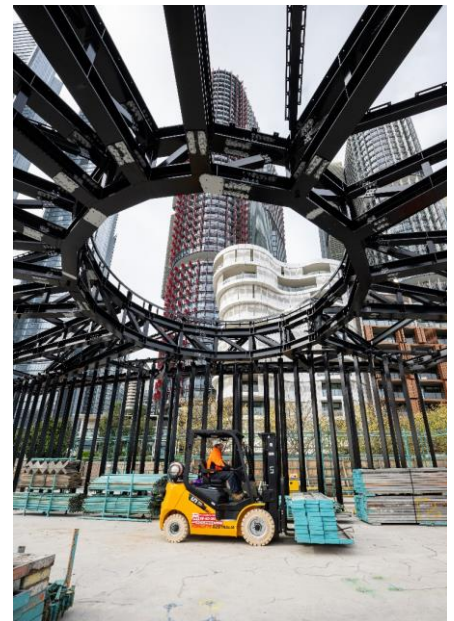

Above: Oculus installed

Upcoming works

In the next few weeks, SEC is:

- Expecting semi-trailer deliveries of Cross Laminated Timber (CLT) for the roof deck structure.
- Installing a medium sized mobile crane.
- Installing the CLT roof deck.
- Roofing activities including installation of roof safety equipment and waterproofing.
- Erection of the Cella wall structure, which will include deliveries of concrete and concrete pumping.

What to expect

During oversized truck deliveries, an exclusion zone will be placed around the semi-trailer, marked by barriers. These zones will be in place for around 4-5 hours on the day of delivery and removed soon after. Truck deliveries are expected around twice a week.

Pedestrian movements will continue to be diverted around the vehicle exclusion zone, and cyclists will be asked to dismount for a small section of Wulugul Walk. SEC will provide signage and traffic controllers will be onsite during certain times to assist.

Working hours

Construction will continue to occur during standard City of Sydney construction hours, with an extended respite period from high noise emission appliances, detailed below. Other plant and machinery will continue during those hours.

Day	Hours of work
Monday to Friday	7.30am - 5.30pm. Respite period: High noise emission appliances*, plant and/or machinery will not be used between 12pm and 2pm.
Saturday	7.30am - 3.30pm. Respite period: High noise emission appliances*, plant and/or machinery will not be used before 9:30am or after 12pm.

*High noise emission appliances include machinery such as piledrivers, rock breakers and hydraulic hammers.

Learn more

- Pier Pavilion [webpage](#)
- Noticeboard for [Community and neighbours](#) updated with construction updates, where required
- For regular Barangaroo development and construction updates, [subscribe](#) to the mailing list.

Contact us

We are committed to keeping you informed and regular updates will be provided.

Contact us for construction-related questions, feedback or complaints:

 1800 679 121
  barangaroo.info@infrastructure.nsw.gov.au
 barangaroo.com

For development updates, [subscribe](#) to the Barangaroo mailing list.

If you need an interpreter, please call Translating and Interpreting Service (TIS) National on 13 14 50 and ask them to call Infrastructure NSW on 1800 679 121 (between 8:30am – 5pm)
